












































































ID		Task Mode	WBS	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Cost
1			A	Construction of 4 bedroom duplex	95.13 days	November 1, 2021	February 22, 2022			₱ 388,875.00
2			A.10	Meeting	94.13 days	November 2, 2021	February 22, 2022			₱ 16,875.00
3	 		A.10.1	Meeting 1	1 hr	November 2, 2021	November 2, 2021		Director,Engineer,Project	₱ 1,875.00
4			A.10.2	Meeting 2	1 hr	November 16, 2021	November 16, 2021		Director,Engineer,Project	₱ 1,875.00
5			A.10.3	Meeting 3	1 hr	November 30, 2021	November 30, 2021		Director,Engineer,Project	₱ 1,875.00
6			A.10.4	Meeting 4	1 hr	December 14, 2021	December 14, 2021		Director,Engineer,Project	₱ 1,875.00
7			A.10.5	Meeting 5	1 hr	December 28, 2021	December 28, 2021		Director,Engineer,Project	₱ 1,875.00
8			A.10.6	Meeting 6	1 hr	January 11, 2022	January 11, 2022		Director,Engineer,Project	₱ 1,875.00
9			A.10.7	Meeting 7	1 hr	January 25, 2022	January 25, 2022		Director,Engineer,Project	₱ 1,875.00
10			A.10.8	Meeting 8	1 hr	February 8, 2022	February 8, 2022		Director,Engineer,Project	₱ 1,875.00
11			A.10.9	Meeting 9	1 hr	February 22, 2022	February 22, 2022		Director,Engineer,Project	₱ 1,875.00
12			A.1	Site Preparation	2.73 days	November 1, 2021	November 3, 2021			₱ 22,000.00
13			A.1.1	Site Clearance	0.33 days	November 1, 2021	November 1, 2021		Labourer[3]	₱ 2,000.00
14			A.1.2	Soil test	1 day	November 1, 2021	November 2, 2021	13	Engineer	₱ 5,000.00
15			A.1.3	Setting out	1 day	November 2, 2021	November 3, 2021	14	Engineer,Labourer	₱ 7,000.00
16			A.1.4	Excavation of trenches	0.4 days	November 3, 2021	November 3, 2021	15	Labourer[5]	₱ 4,000.00
17			A.1.5	Excavation of column bases	0.4 days	November 3, 2021	November 3, 2021	15	Labourer[5]	₱ 4,000.00
18			A.2	Substructure	10.9 days	November 2, 2021	November 15, 2021			₱ 57,000.00
19			A.2.1	Blinding of foundation	2 days	November 3, 2021	November 5, 2021	16	Bricklayer,Labourer[4]	₱ 10,000.00
20			A.2.2	Preparation of starter bar/basket	3 days	November 2, 2021	November 5, 2021	17FF		₱ 0.00

Project: ASSIGNMENT NO 2 (PRED Date: October 18, 2021)

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID		Task Mode	WBS	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Cost
21			A.2.3	Blockwork in foundation	2.5 days	November 5, 2021	November 9, 2021	19	Bricklayer[2],Labourer[2]	₺ 20,000.00
22			A.2.4	Casting of starter bars/basket	1 day	November 8, 2021	November 9, 2021	20,21FF	Labourer[2]	₺ 4,000.00
23			A.2.5	Backfilling of trenches	1 day	November 9, 2021	November 10, 2021	22	Labourer[3]	₺ 6,000.00
24			A.2.6	Laying of hardcore	1 day	November 10, 2021	November 11, 2021	23	Labourer	₺ 2,000.00
25			A.2.7	Casting of oversite concrete	3 days	November 11, 2021	November 15, 2021	24	Bricklayer,Labourer[7],M	₺ 15,000.00
26			A.3	Superstructure	26.75 days	November 15, 2021	December 15, 2021			₺ 149,000.00
27			A.3.1	Blockwork in groundfloor (floor to lintel)	3.5 days	November 15, 2021	November 18, 2021	25	Bricklayer[2],Labourer[2]	₺ 28,000.00
28			A.3.2	Preparation of column/lintel/be rebar	4 days	November 15, 2021	November 19, 2021	25		₺ 0.00
29			A.3.3	Casting of ground floor columns	1.67 days	November 19, 2021	November 20, 2021	28	Labourer[3]	₺ 10,000.00
30			A.3.4	Casting of lintels	1.33 days	November 20, 2021	November 23, 2021	29	Labourer[3]	₺ 8,000.00











Project: ASSIGNMENT NO 2 (PRED Date: October 18, 2021)

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	



















ID	Task Mode	WBS	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Cost
31		A.3.5	Blockwork (lintel to first floor)	1 day	November 23, 2021	November 24, 2021	30	Bricklayer[2],Labourer[2]	₺ 8,000.00
32		A.3.6	Formwork for suspended floor/beam	1.5 days	November 27, 2021	November 29, 2021	31FS+3 days	Carpenter[4]	₺ 18,000.00
33		A.3.7	Preparation of concrete spacer	1 day	November 24, 2021	November 25, 2021	31	Labourer	₺ 2,000.00
34		A.3.8	Casting of first floor columns/beams	0.75 days	November 29, 2021	November 30, 2021	32	Labourer[4]	₺ 6,000.00
35		A.3.9	Blockwork in first floor to lintels	7 days	November 30, 2021	December 8, 2021	34	Bricklayer,Labourer	₺ 35,000.00
36		A.3.10	Casting of first floor columns	1 day	December 8, 2021	December 9, 2021	35	Labourer[4]	₺ 8,000.00
37		A.3.11	Blockwork (lintel to roof beams)	4 days	December 9, 2021	December 14, 2021	36	Bricklayer,Labourer	₺ 20,000.00
38		A.3.12	Casting of roof beams	1.5 days	December 14, 2021	December 15, 2021	37	Labourer[2]	₺ 6,000.00
39		A.4	Roofing	2.25 days	December 18, 2021	December 22, 2021			₺ 27,000.00
40		A.4.1	Installation of roof carcass	1.25 days	December 18, 2021	December 21, 2021	38FS+3 days	Carpenter[4]	₺ 15,000.00


Project: ASSIGNMENT NO 2 (PRED Date: October 18, 2021)

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID		Task Mode	WBS	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Cost
41			A.4.2	Installation of roof sheets	1 day	December 21, 2021	December 22, 2021	40	Carpenter[4]	₺ 12,000.00
42			A.5	Frames	3 days	December 22, 2021	December 27, 2021			₺ 18,000.00
43			A.5.1	Installation of doors	1.5 days	December 22, 2021	December 23, 2021	41	Carpenter[2],Door[10 Units]	₺ 9,000.00
44			A.5.2	Installation of windows	1.5 days	December 23, 2021	December 27, 2021	43	Carpenter[2],Window[10 Units]	₺ 9,000.00
45			A.6	Fittings	3 days	December 22, 2021	December 27, 2021			₺ 24,000.00
46			A.6.1	Mechanical fittings	3 days	December 22, 2021	December 27, 2021	41	Plumber	₺ 9,000.00
47			A.6.2	Electrical fittings	3 days	December 22, 2021	December 27, 2021	41	Engineer	₺ 15,000.00
48			A.7	Finishes	26.62 days	December 27, 2021	January 27, 2022			₺ 75,000.00
49			A.7.1	Plastering	2.5 days	December 27, 2021	December 29, 2021	47	Bricklayer[2],Labourer[2]	₺ 20,000.00
50			A.7.2	Painting	5 days	December 29, 2021	January 6, 2022	49	Painter,Paint brush[1 Units],Paint[1 Gallons]	₺ 15,000.00
51			A.7.3	General Cleaning	2.86 days	January 13, 2022	January 27, 2022		Labourer[7]	₺ 40,000.00
52			A.8	Interior decoration	8 days	January 6, 2022	January 15, 2022	50		₺ 0.00
53			A.9	Commissioning and handover	1 day	January 15, 2022	January 17, 2022	52		₺ 0.00


Project: ASSIGNMENT NO 2 (PRED
Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

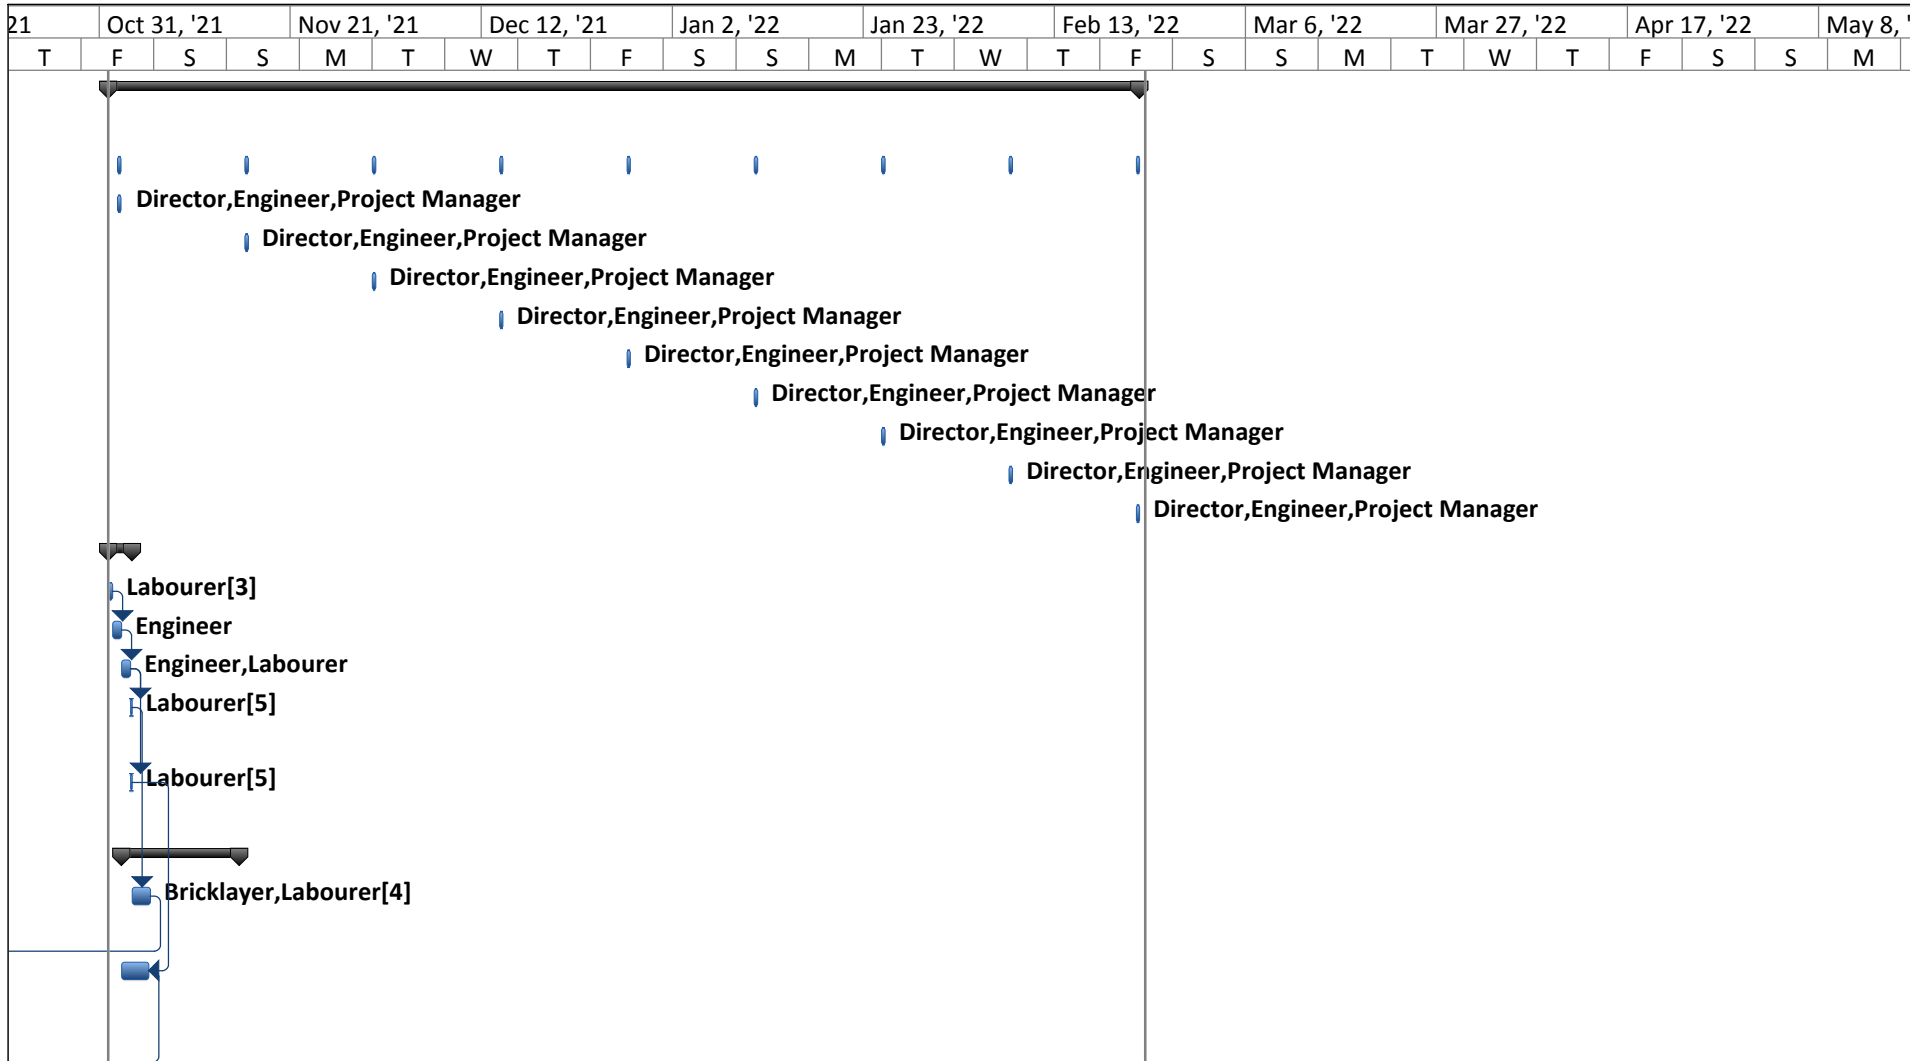


Project: ASSIGNMENT NO 2 (PRED)
Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

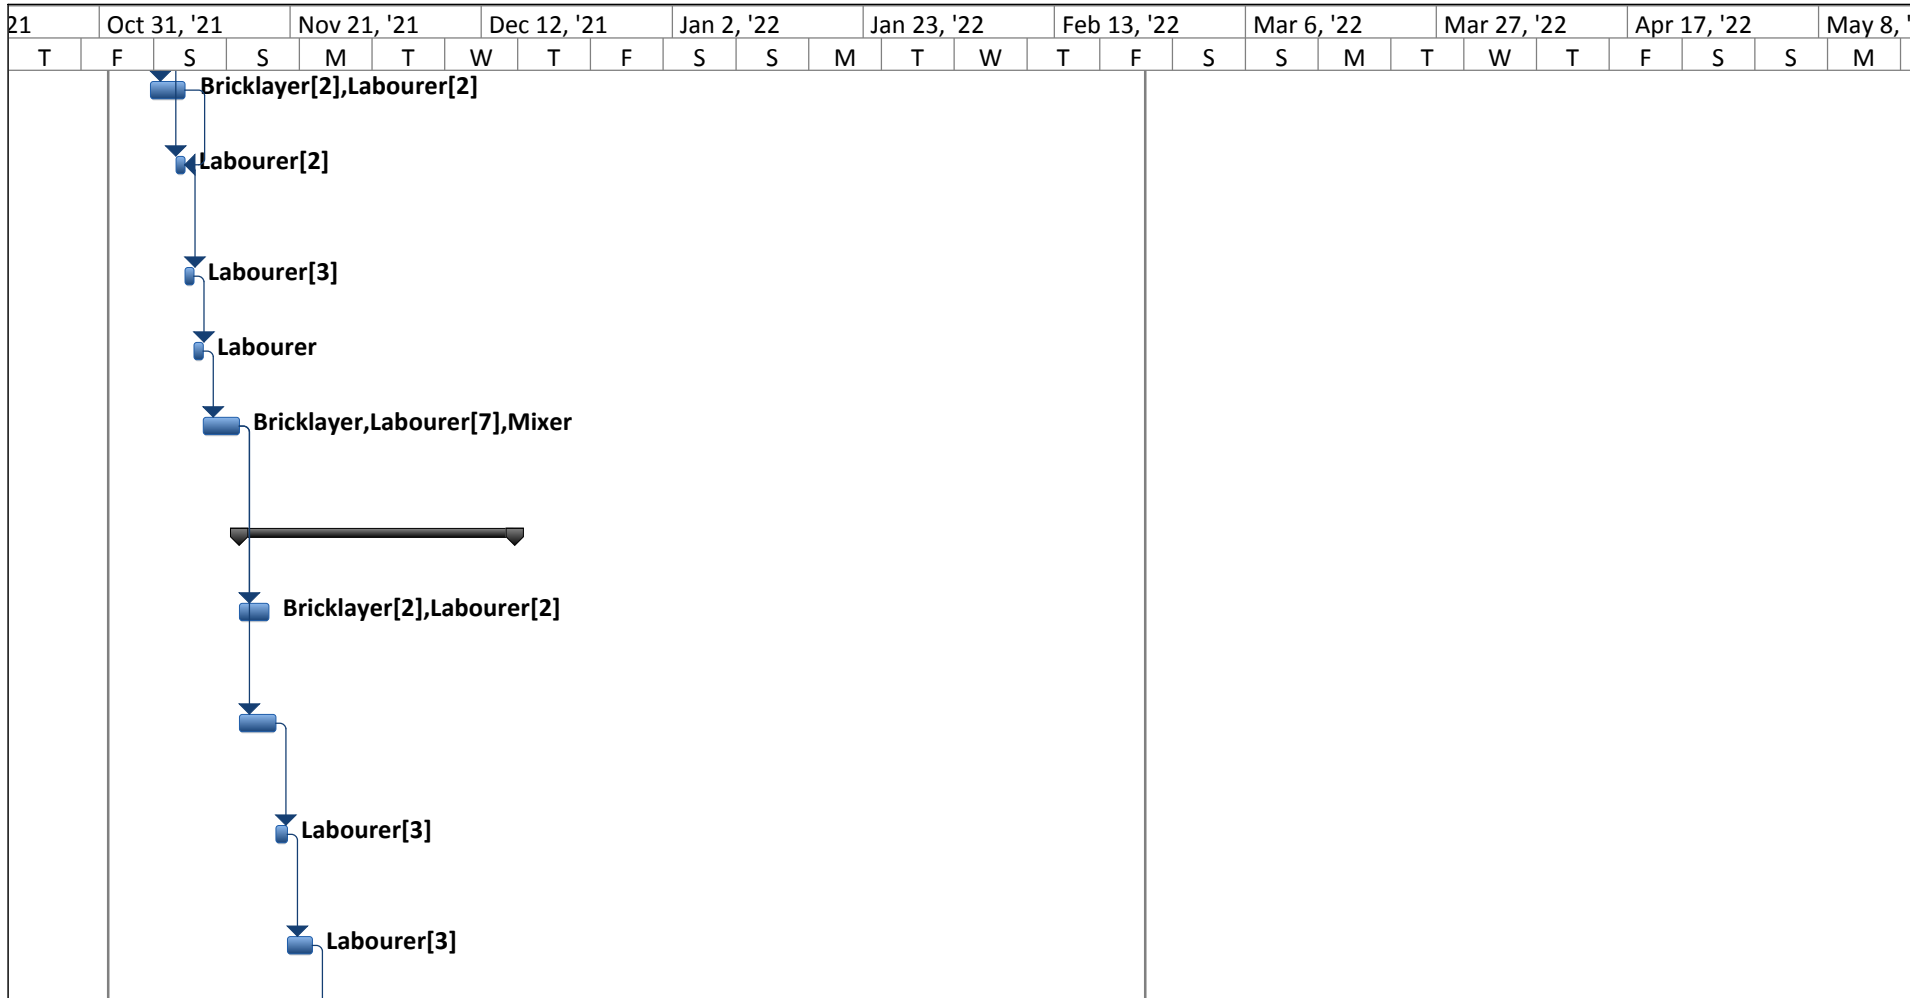


Project: ASSIGNMENT NO 2 (PRED)
Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

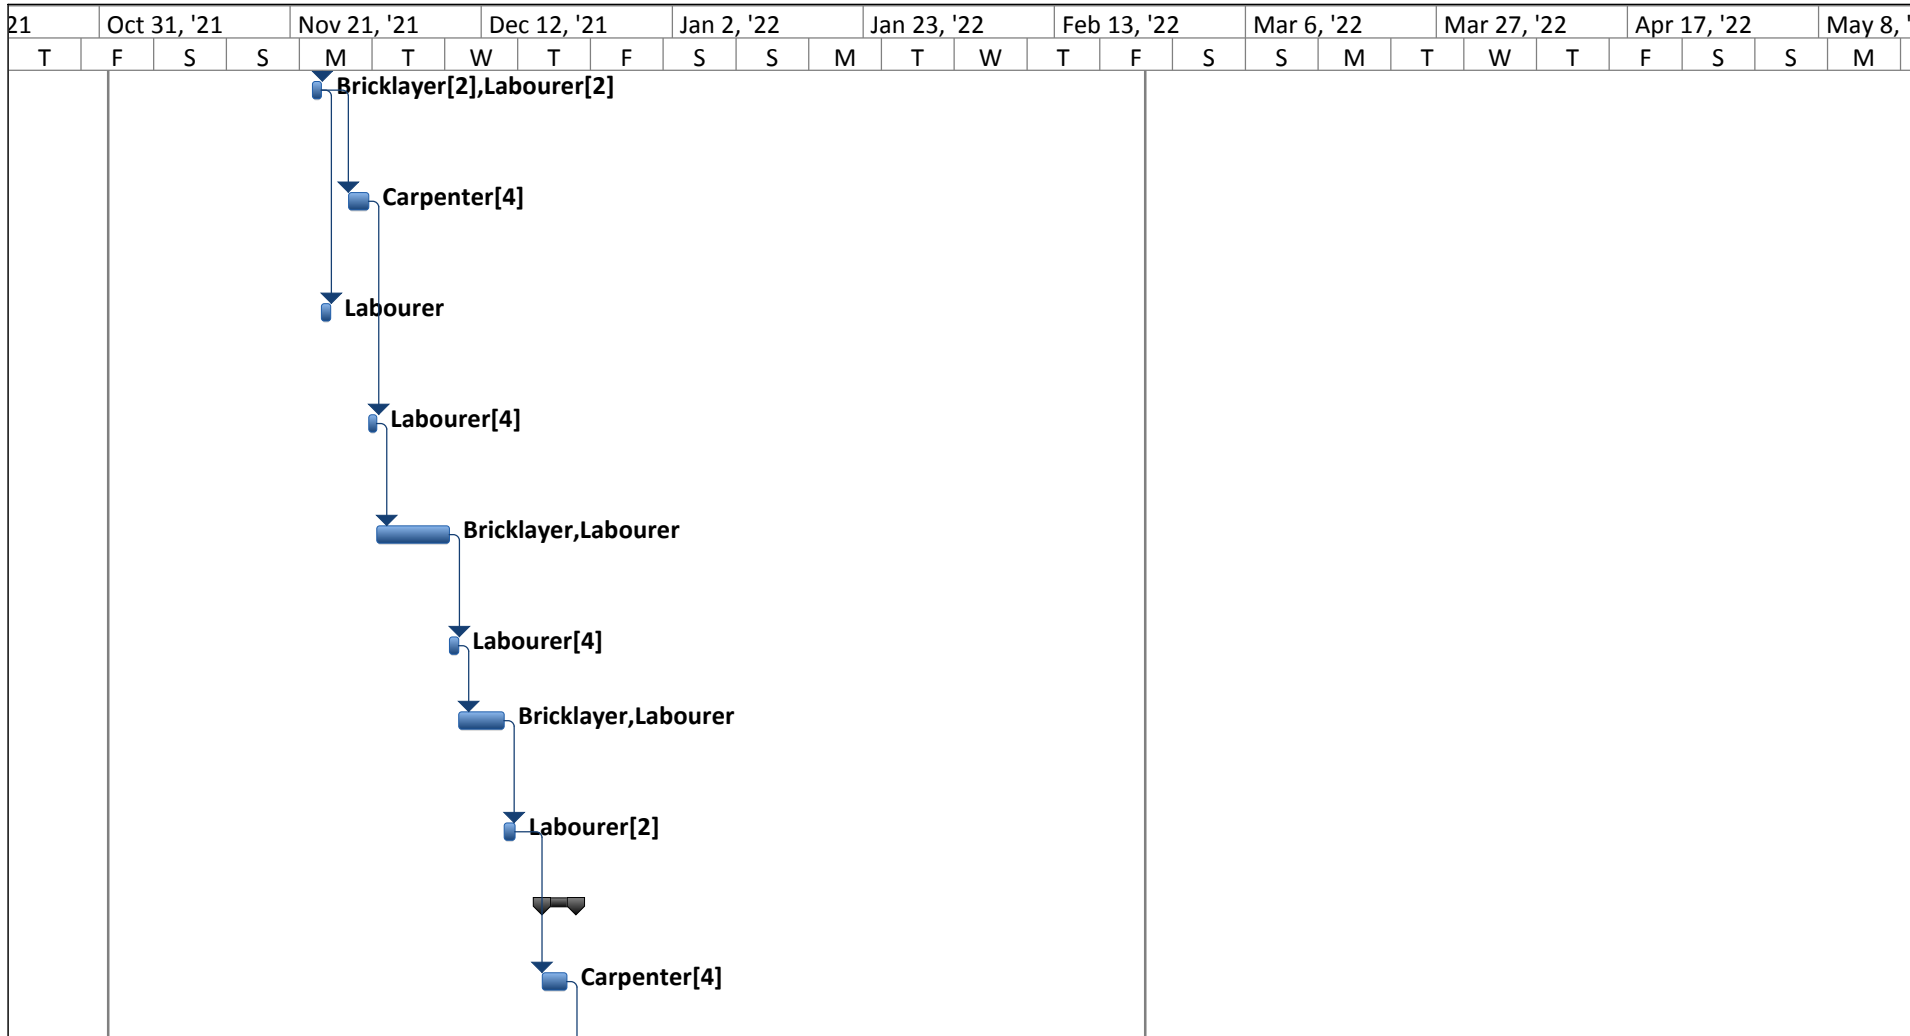

Project: ASSIGNMENT NO 2 (PRED)
Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

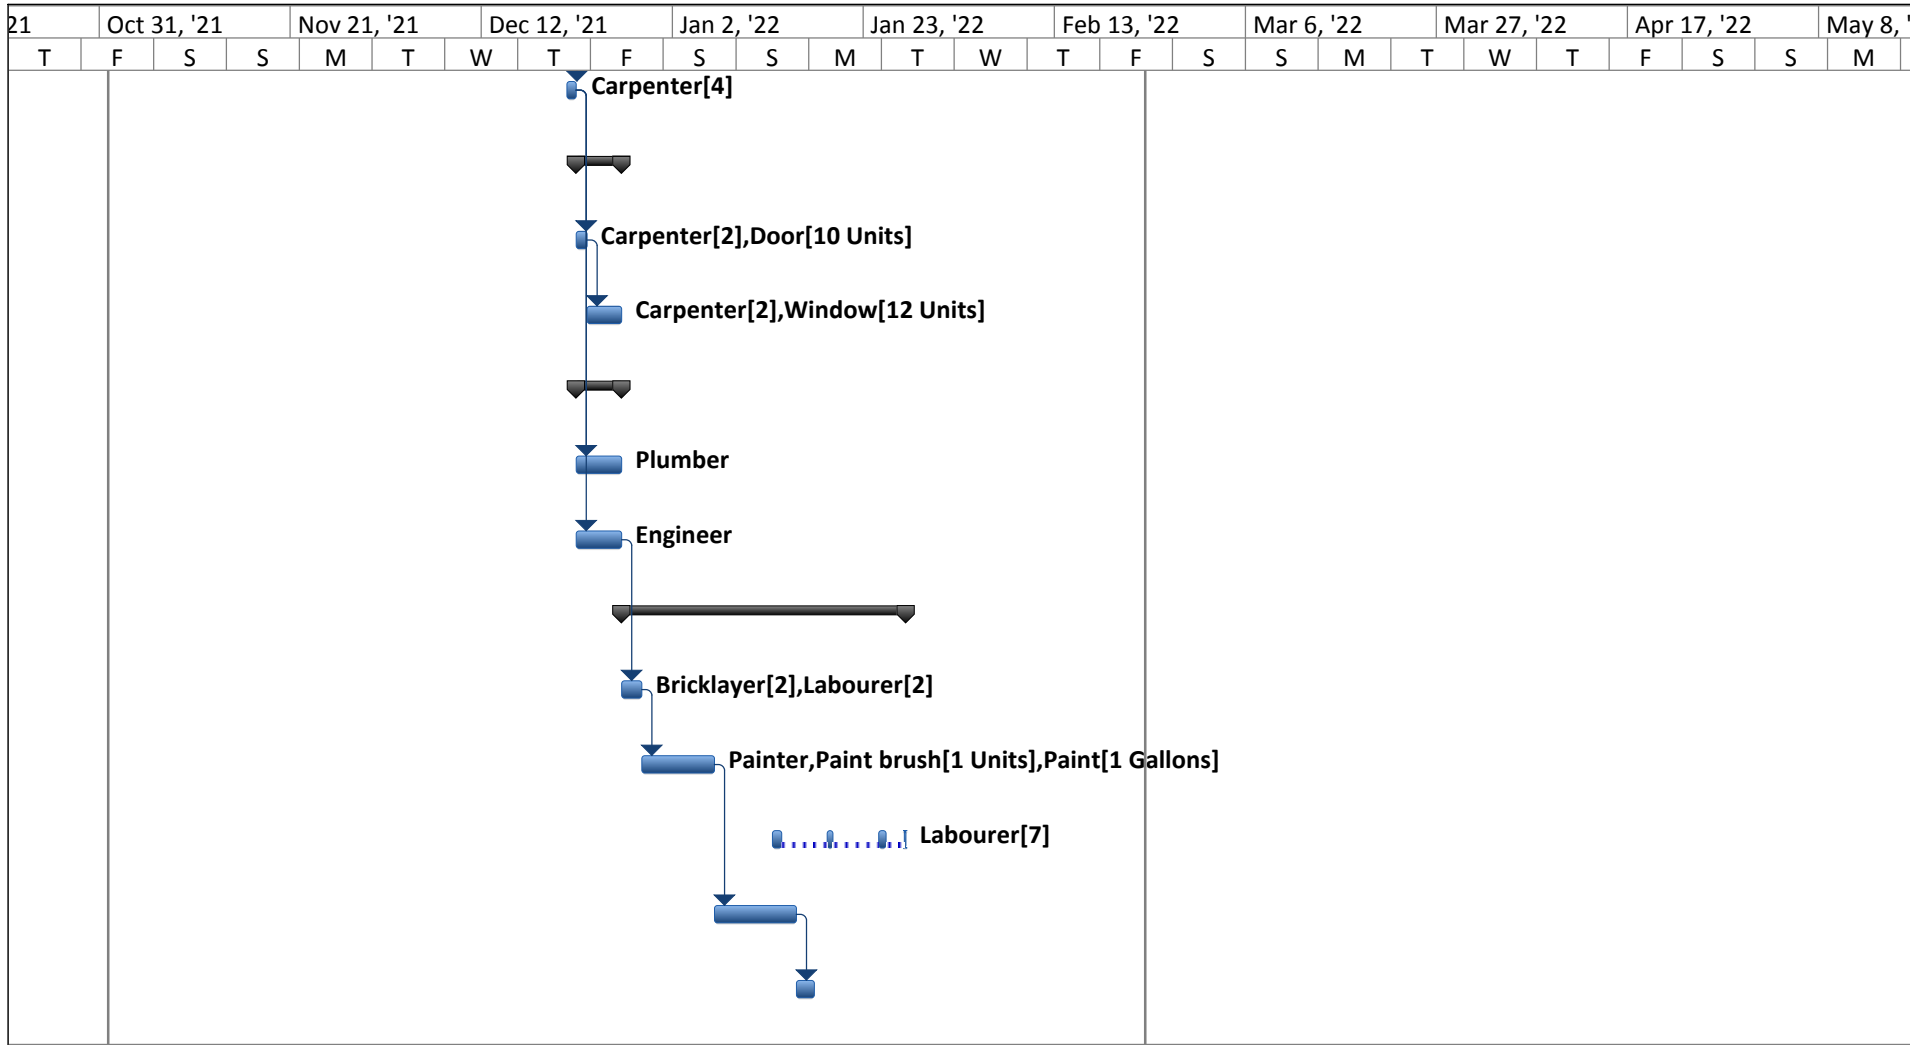

Project: ASSIGNMENT NO 2 (PRED)
Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	
