


ID	Task Name	Duration	Start	Finish	Predecessors	Oct 31, '21							Nov 7, '21							
						S	S	M	T	W	T	F	S	S	M	T	W	T	F	S
1	Construction of 4 bedroom duplex	98 days	November 1, 2021	February 24, 2022																
2	Meeting	94.13 days	November 2, 2021	February 22, 2022																
3	Meeting 1	1 hr	November 2, 2021	November 2, 2021																
4	Meeting 2	1 hr	November 16, 2021	November 16, 2021																
5	Meeting 3	1 hr	November 30, 2021	November 30, 2021																
6	Meeting 4	1 hr	December 14, 2021	December 14, 2021																
7	Meeting 5	1 hr	December 28, 2021	December 28, 2021																
8	Meeting 6	1 hr	January 11, 2022	January 11, 2022																
9	Meeting 7	1 hr	January 25, 2022	January 25, 2022																
10	Meeting 8	1 hr	February 8, 2022	February 8, 2022																
11	Meeting 9	1 hr	February 22, 2022	February 22, 2022																
12	Site Preparation	5 days	November 1, 2021	November 5, 2021																
13	Site Clearance	1 day	November 1, 2021	November 1, 2021																
14	Soil test	1 day	November 2, 2021	November 2, 2021	13															
15	Setting out	1 day	November 3, 2021	November 3, 2021	14															
16	Excavation of trenches	2 days	November 4, 2021	November 5, 2021	15															
17	Excavation of column bases	2 days	November 4, 2021	November 5, 2021	15															
18	Substructure	17 days	November 3, 2021	November 22, 2021																
19	Blinding of foundation	2 days	November 6, 2021	November 8, 2021	16															
20	Preparation of starter bar/basket	3 days	November 3, 2021	November 5, 2021	17FF															

Project: ASSIGNMENT NO 2 (PRED
Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	


ID	Task Name	Duration	Start	Finish	Predecessors	Oct 31, '21							Nov 7, '21							
						S	S	M	T	W	T	F	S	S	M	T	W	T	F	S
35	Blockwork in first floor to lintels	7 days	December 24, 2021	January 3, 2022	34															
36	Casting of first floor columns	4 days	January 4, 2022	January 7, 2022	35															
37	Blockwork (lintel to roof beams)	4 days	January 8, 2022	January 12, 2022	36															
38	Casting of roof beam	3 days	January 13, 2022	January 15, 2022	37															
39	Roofing	9 days	January 20, 2022	January 29, 2022																
40	Installation of roof carcass	5 days	January 20, 2022	January 25, 2022	38FS+3 days															
41	Installation of roof sheets	4 days	January 26, 2022	January 29, 2022	40															
42	Frames	6 days	January 31, 2022	February 5, 2022																
43	Installation of doors	3 days	January 31, 2022	February 2, 2022	41															
44	Installation of windows	3 days	February 3, 2022	February 5, 2022	43															
45	Fittings	3 days	January 31, 2022	February 2, 2022																
46	Mechanical fittings	3 days	January 31, 2022	February 2, 2022	41															
47	Electrical fittings	3 days	January 31, 2022	February 2, 2022	41															
48	Finishes	30 days	January 13, 2022	February 16, 2022																
49	Plastering	5 days	February 3, 2022	February 8, 2022	47															
50	Painting	5 days	February 9, 2022	February 14, 2022	49															
51	General Cleaning	20 days	January 13, 2022	February 16, 2022																
52	Interior decoration	8 days	February 15, 2022	February 23, 2022	50															
53	Commissioning and handover	1 day	February 24, 2022	February 24, 2022	52															

Project: ASSIGNMENT NO 2 (PREL) Date: October 18, 2021	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

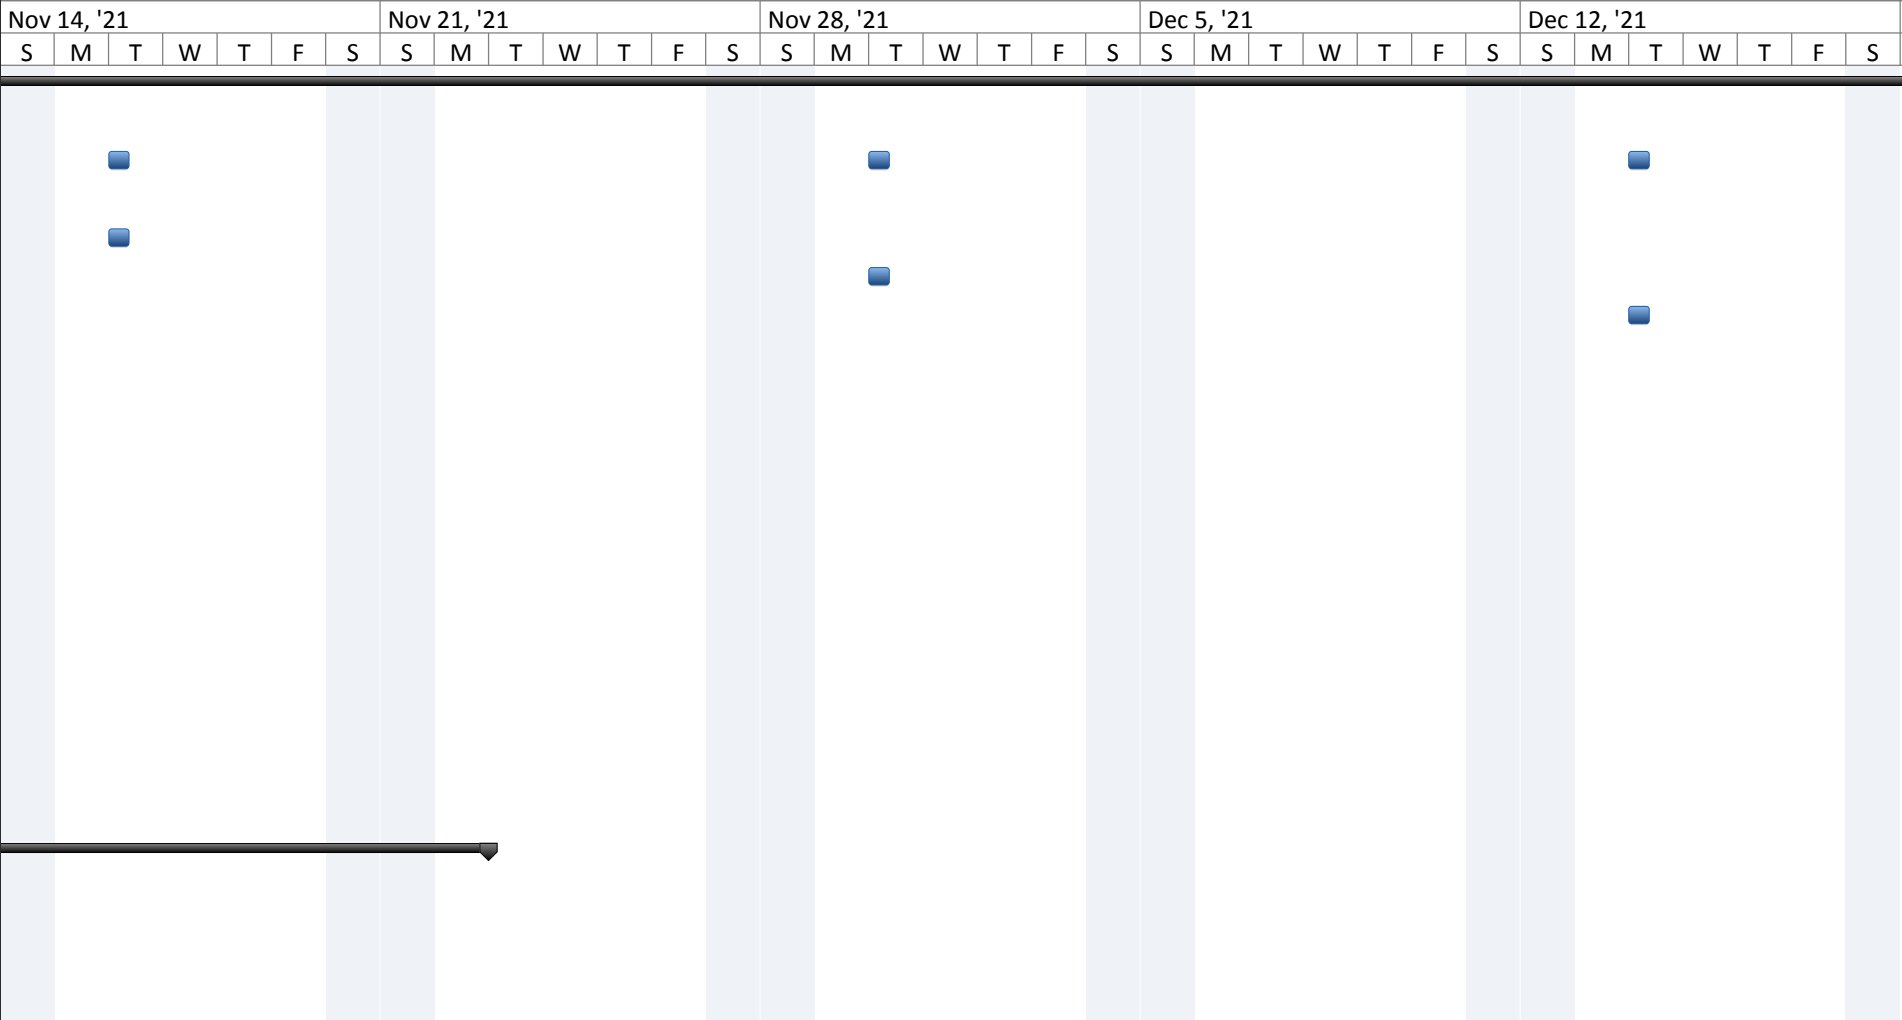


Project: ASSIGNMENT NO 2 (PRED)
Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

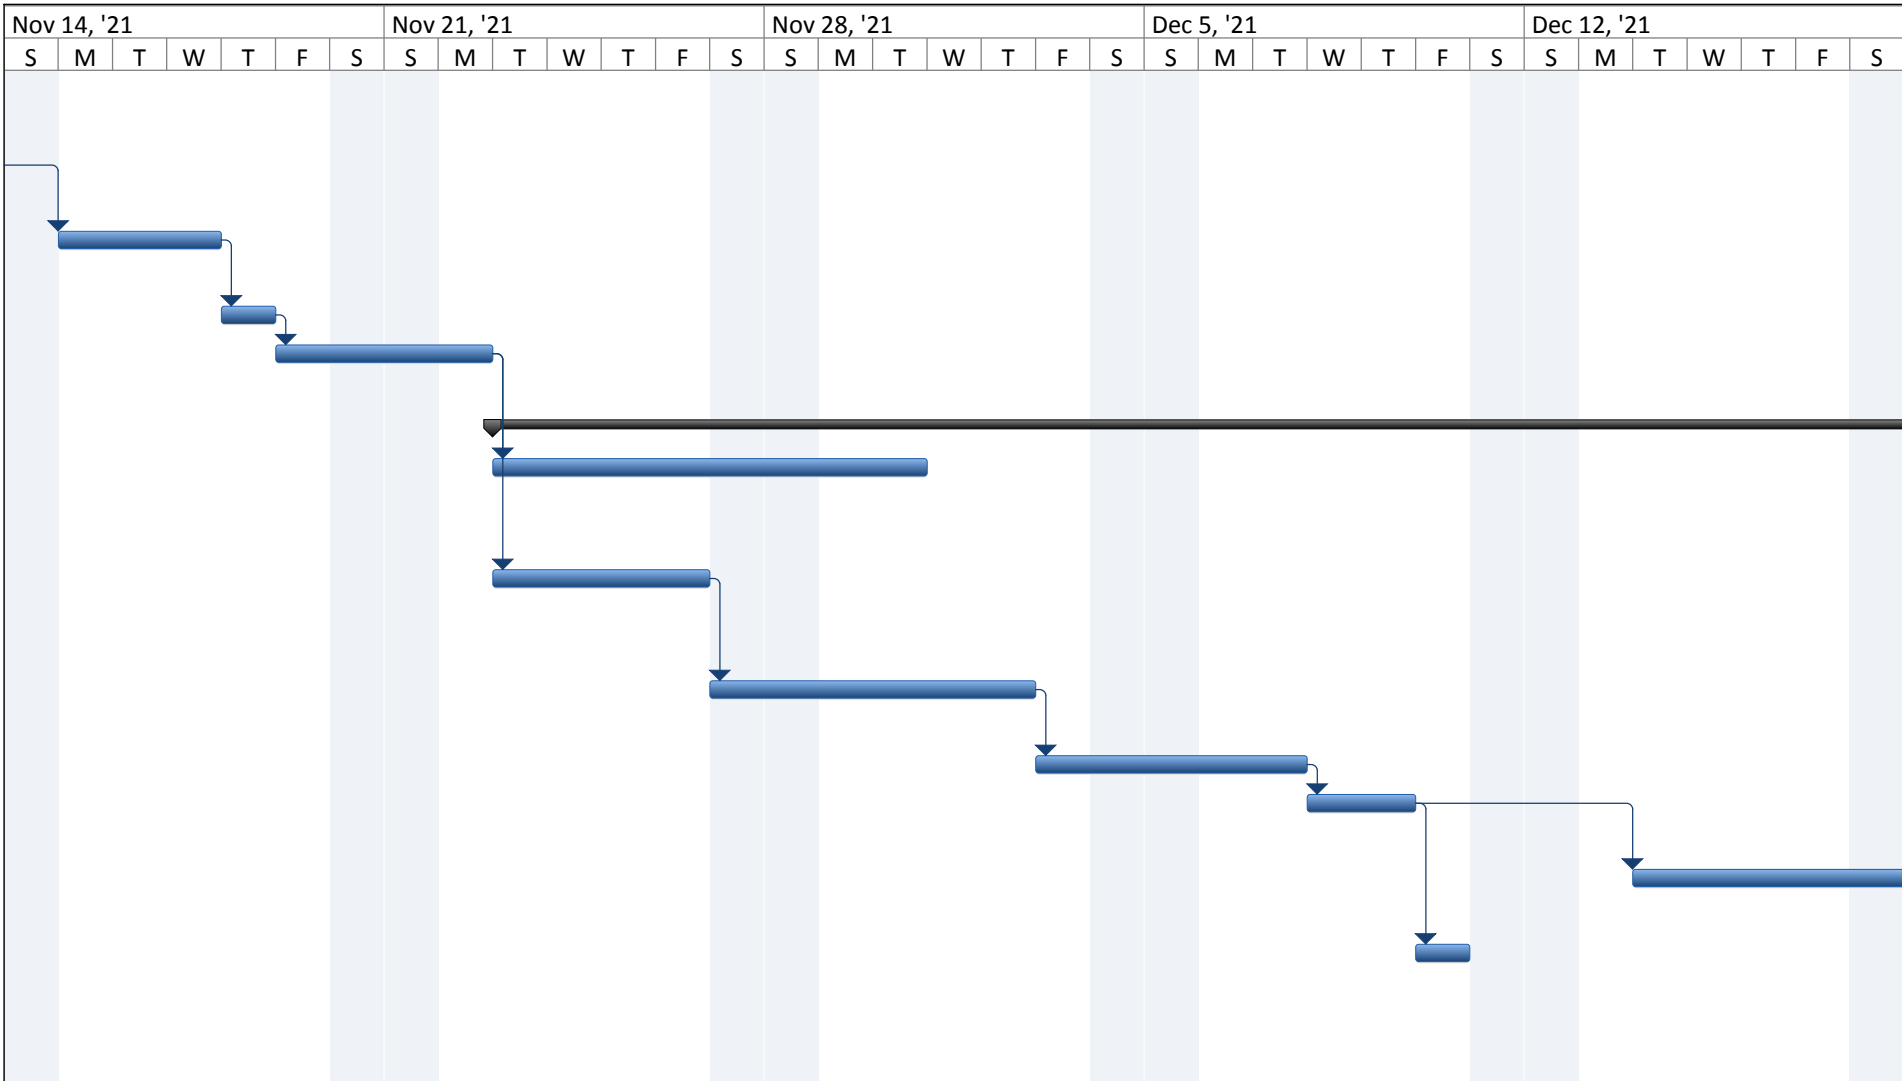


Project: ASSIGNMENT NO 2 (PRED)
 Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	




Project: ASSIGNMENT NO 2 (PRED
Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

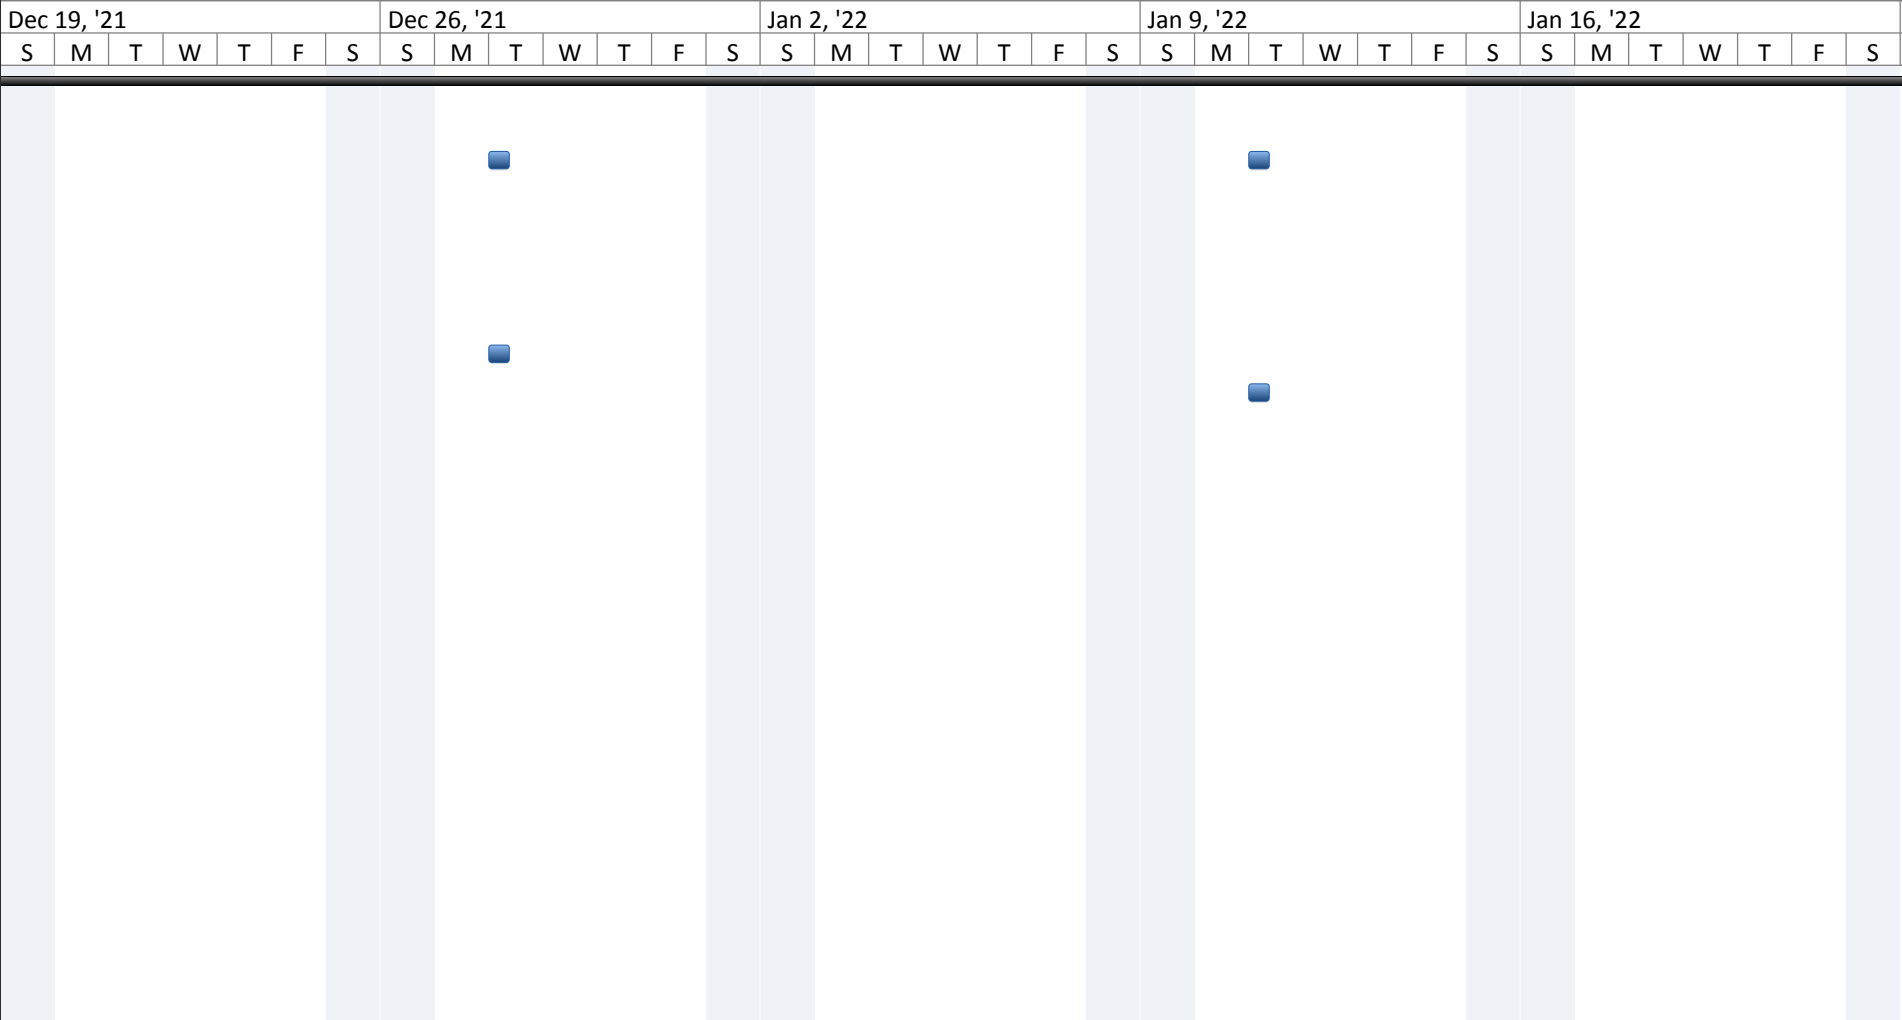


Project: ASSIGNMENT NO 2 (PRED)
 Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

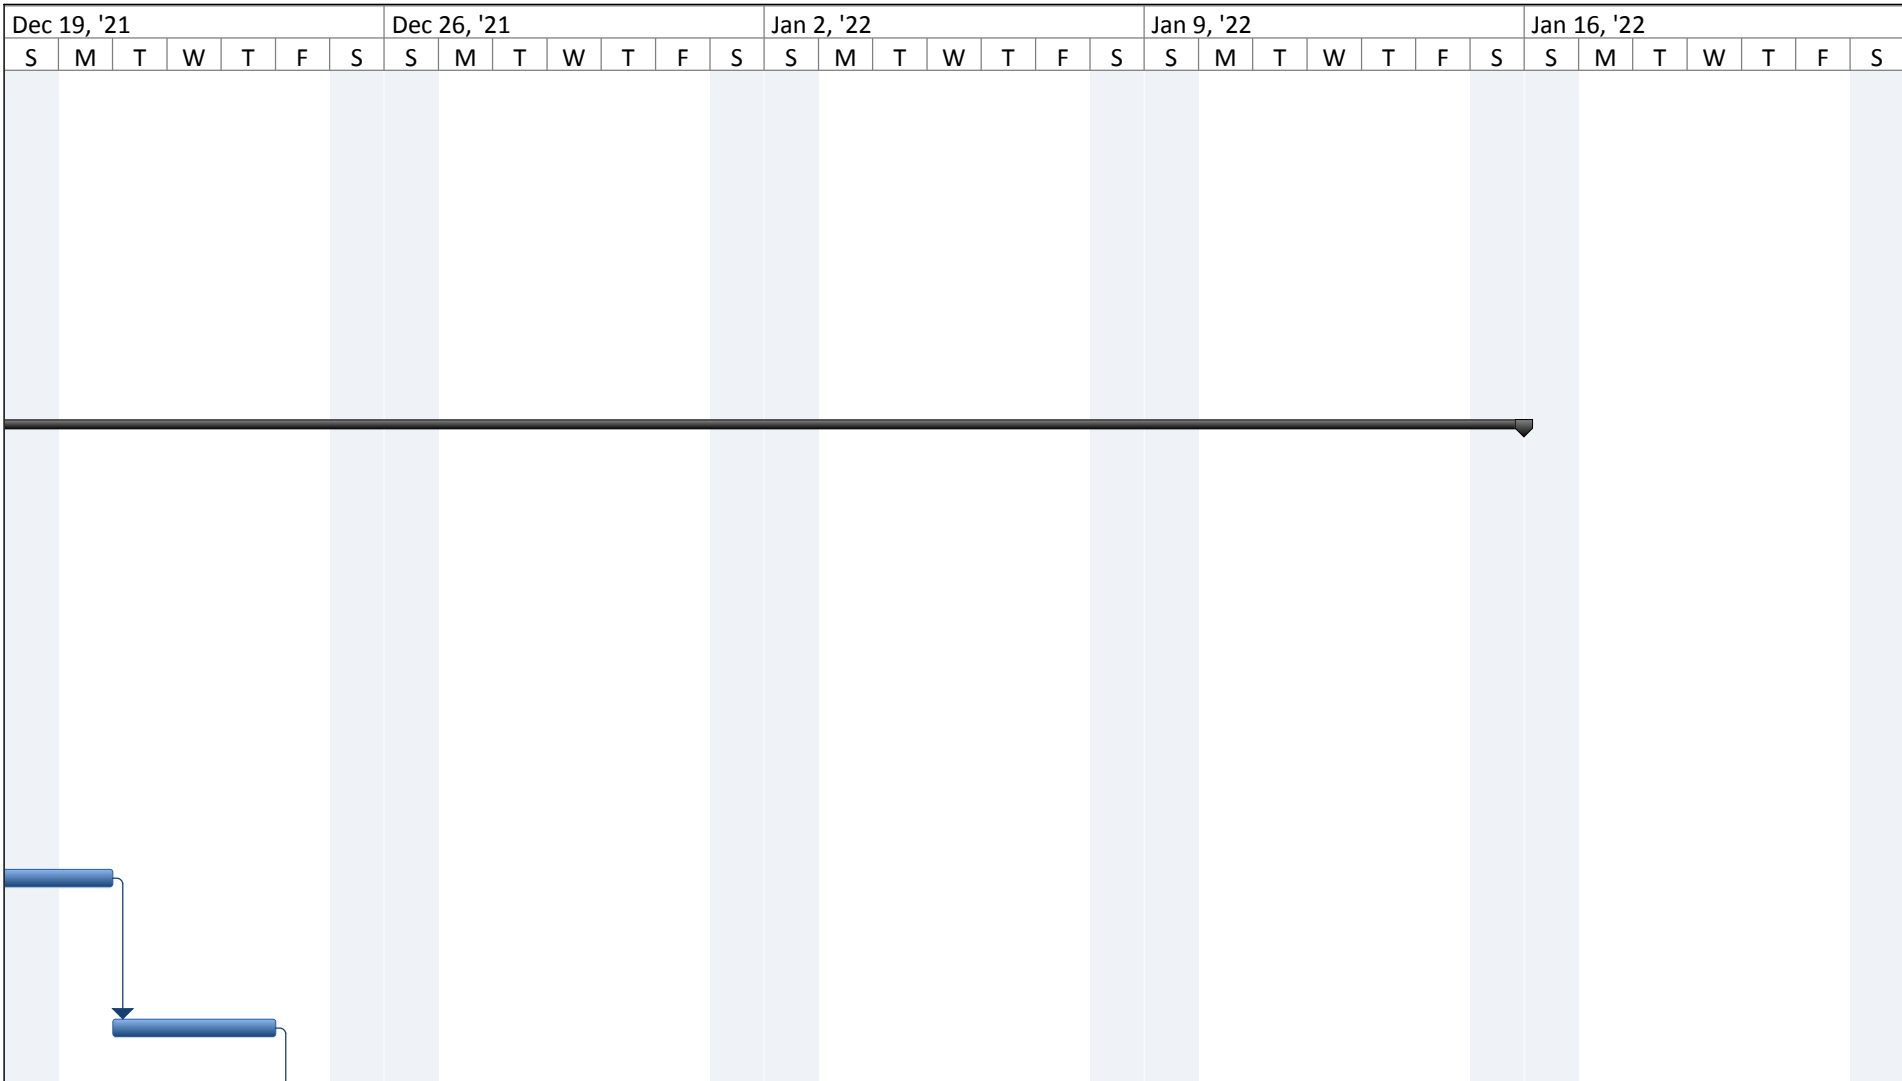


Project: ASSIGNMENT NO 2 (PRED)
Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

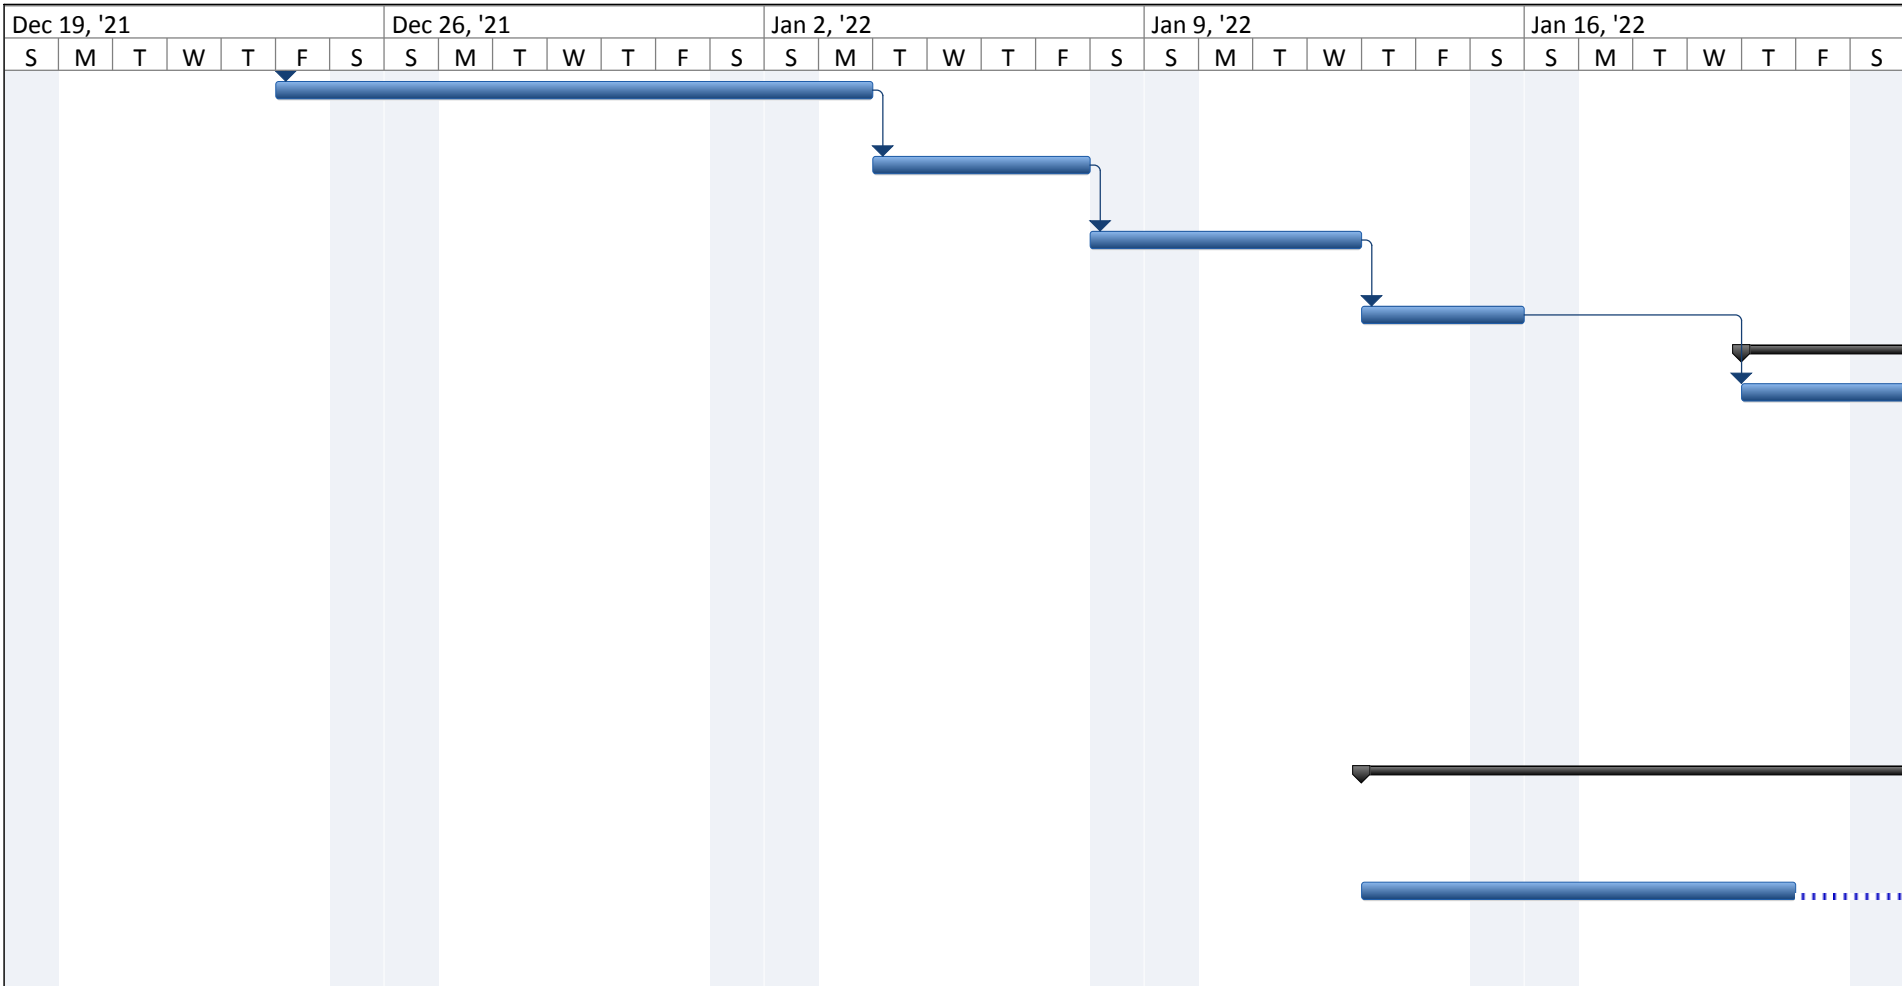


Project: ASSIGNMENT NO 2 (PRED)
Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

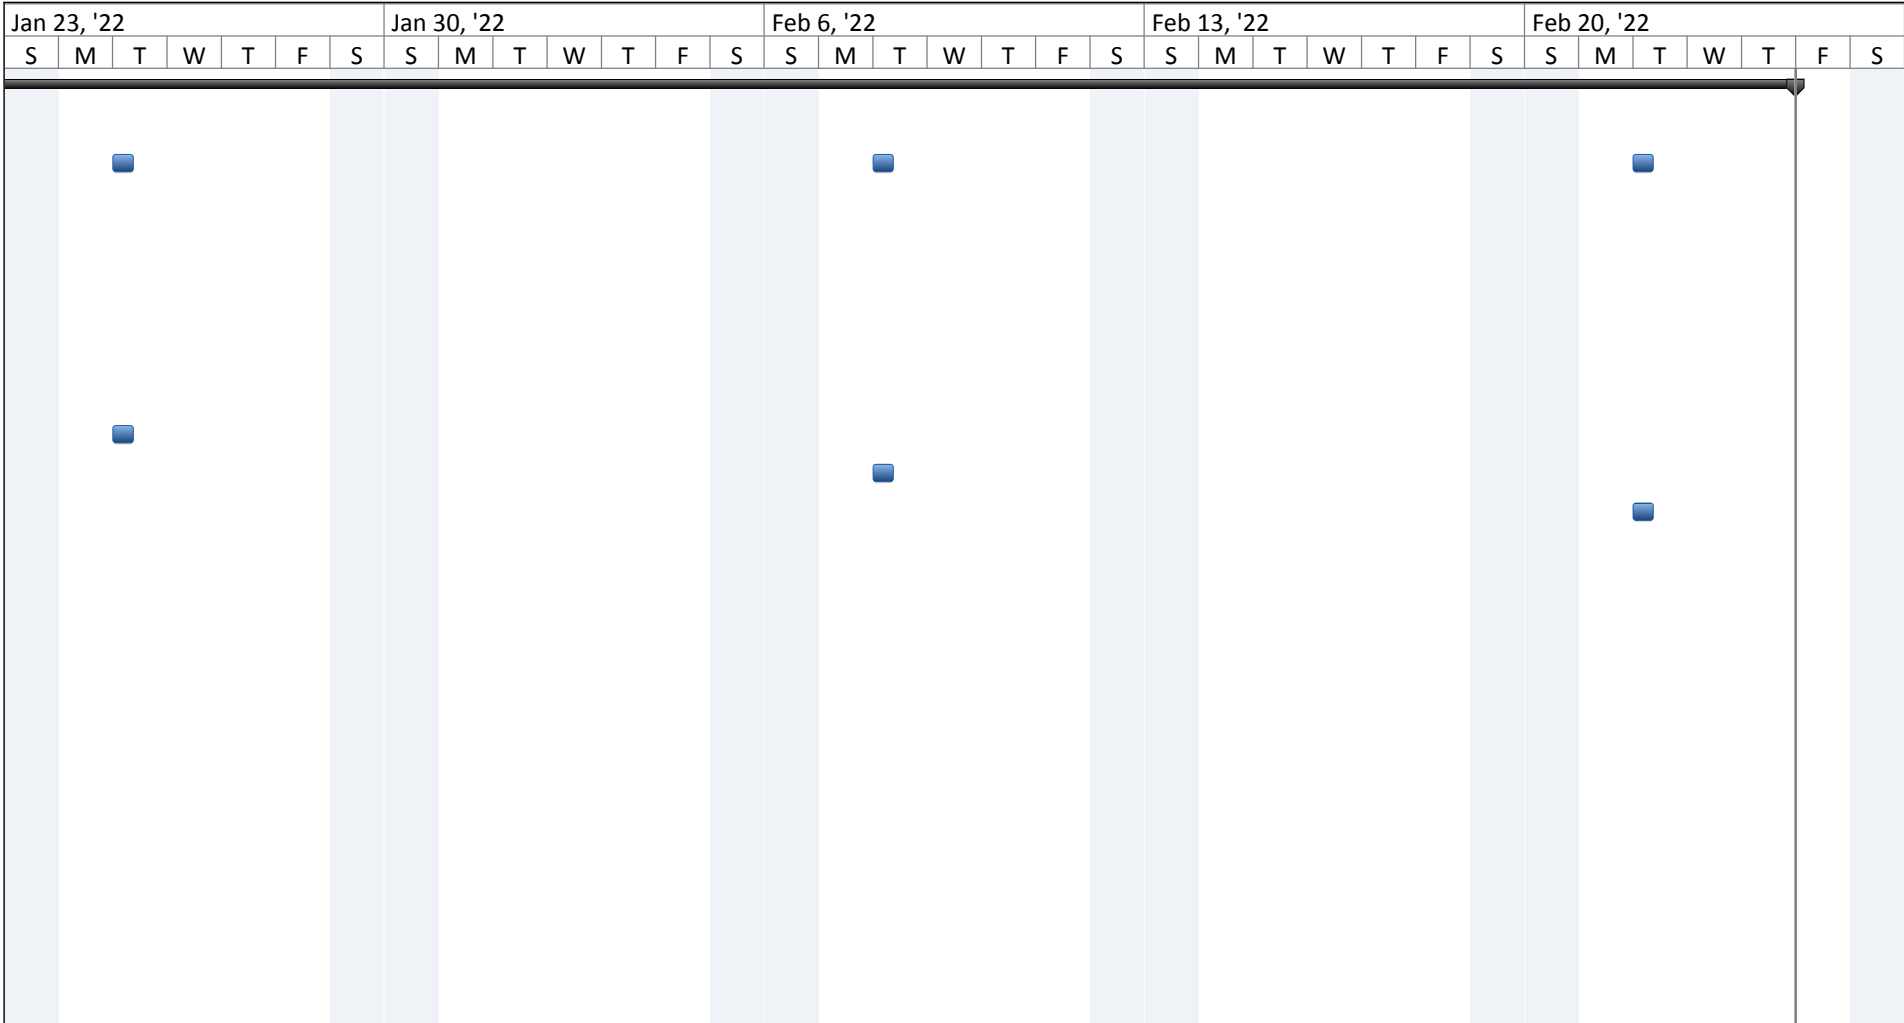





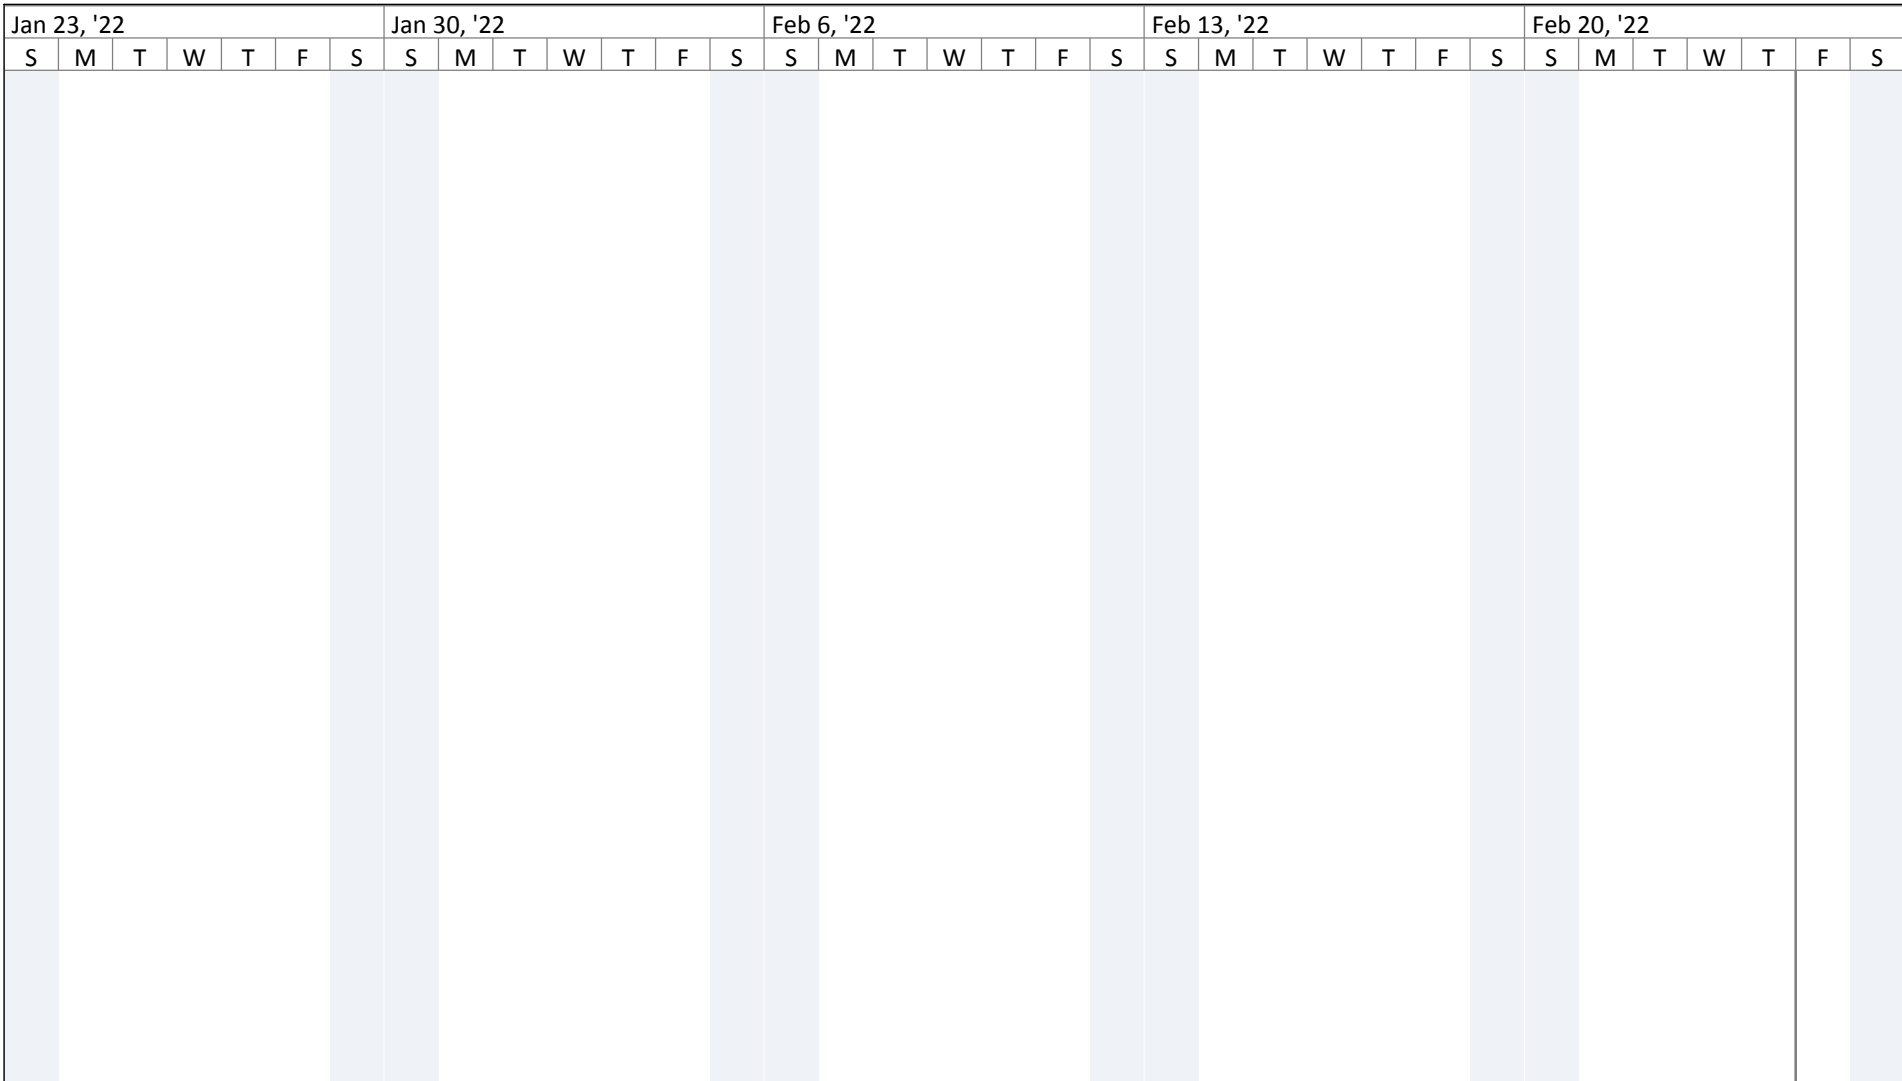














Project: ASSIGNMENT NO 2 (PRED)
Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	



Project: ASSIGNMENT NO 2 (PRED
Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

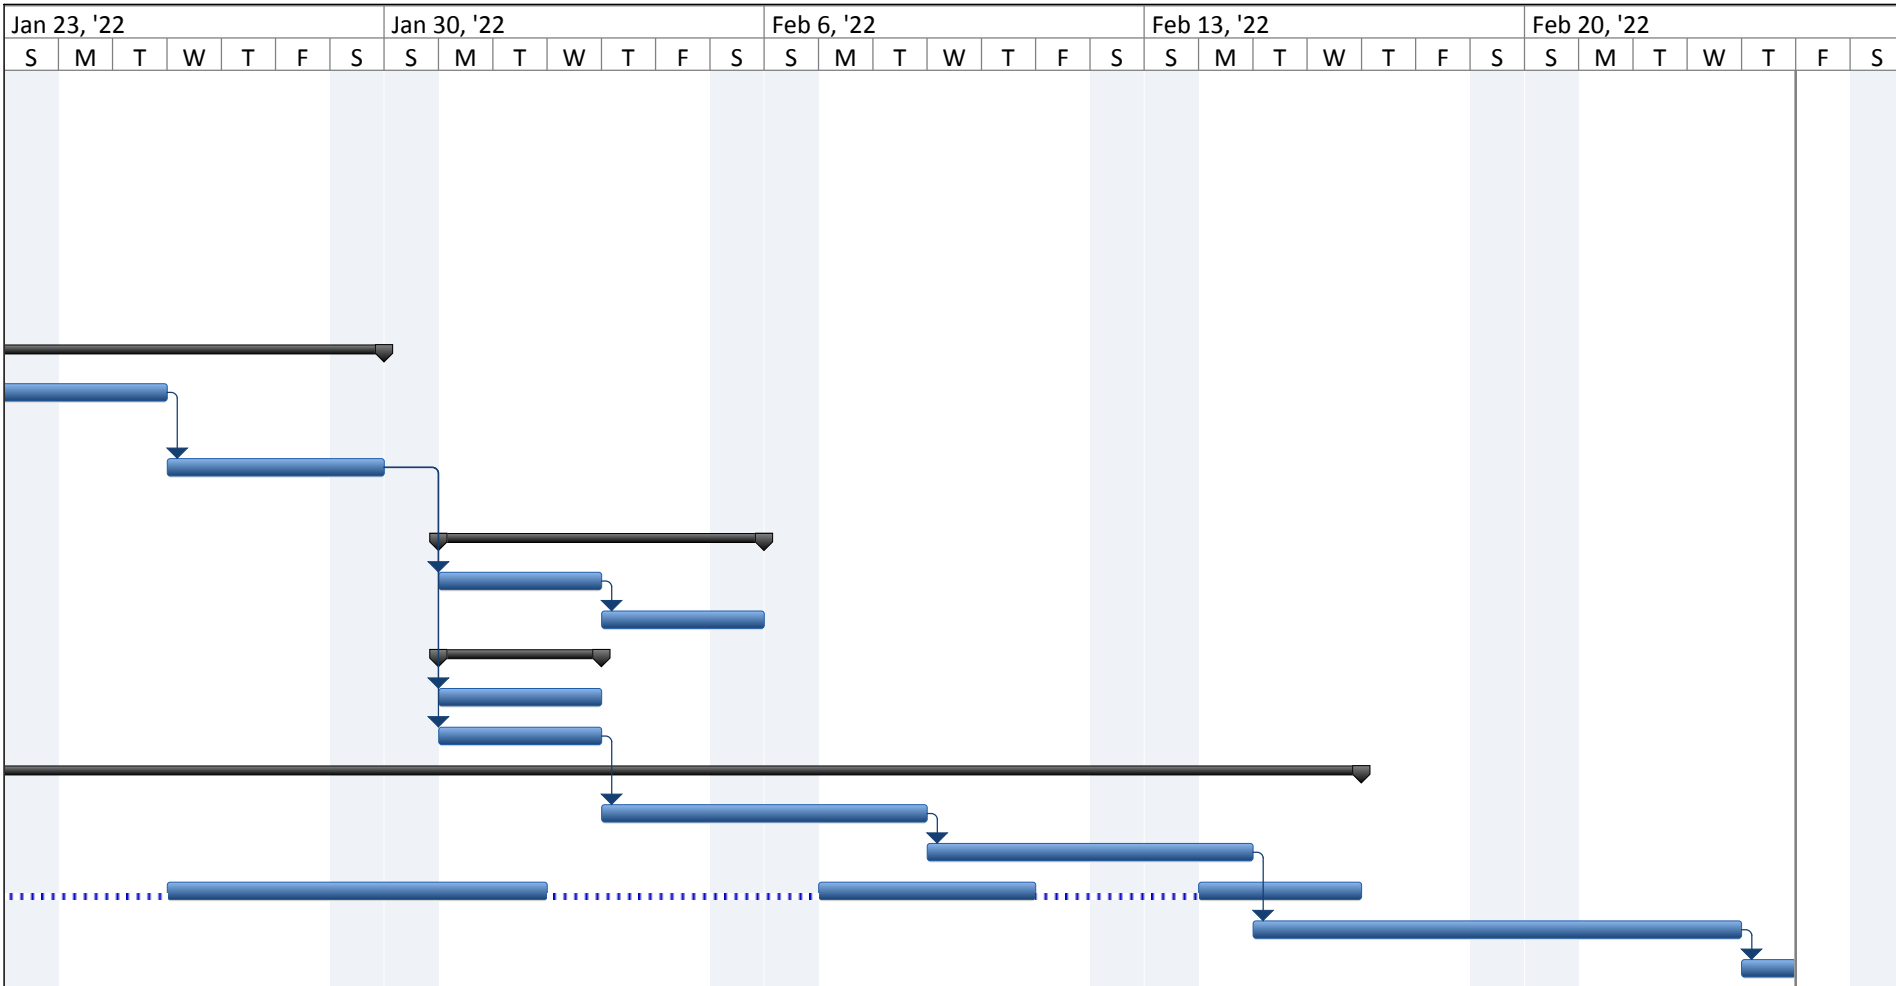

Project: ASSIGNMENT NO 2 (PRED)
 Date: October 18, 2021

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	
